PantriHub

Shared Inventory Platform for Food Banks

Project Scrum / Progress Check-in

March 18, 2026 | ENSE 281

Shivam Soni • Ethan Behl • Thomas Needham • Ishan Patel • Bushra Alkhateeb

Meet the Team

Shivam Soni

Ethan Behl

Bushra Alkhateeb

Thomas Needham

Ishan Patel

Agenda

01 Project Overview & Problem Statement

02 Current Sprint Status (Yellow)

03 What We Accomplished This Week

04 Technical Architecture & Demo

05 Next Week’s Plan & Recovery Strategy

06 Self-Reflection

The Problem

Food banks in Saskatchewan operate in isolation

- No visibility into each other's inventory
- Surplus at one location, shortages at another
- Food waste from uncoordinated expiry tracking
- Manual processes prone to error

PantriHub Solution

A shared dashboard that lets food banks see, search, and coordinate inventory across all locations in real time.

Validated through interviews with food banks in Regina, Calgary, and Vancouver

Sprint Status

YELLOW

Why Yellow?

- Team lead (Shivam) unavailable this week
- All members had final round of midterms
- Sprint 1 (Mar 10–16) behind schedule

Recovery Plan

- Team sync to assign clear ownership
- Compress Sprint 1 + overlap with Sprint 2
- Regular check-ins to catch blockers early

Sprint 1: Auth + CRUD (FR-01–FR-07)	Sprint 2: Dashboard + Search (FR-08–FR-14)
Mar 10–23 (extended)	Mar 17–23 (overlapping)

This Week's Progress

Ishan & Bushra

Frontend

Sign Up & Registration page
(FR-01, FR-02)
HTML/Bootstrap layouts

Ethan

Backend

MongoDB database setup
Connection configuration

Thomas

Backend

Helping Ethan setting up the environment

Shivam

Team Lead / Flex

Unavailable last week
Resuming this week

Project scaffolding complete: Node.js/Express initialized with MVC folder structure

MVC Architecture

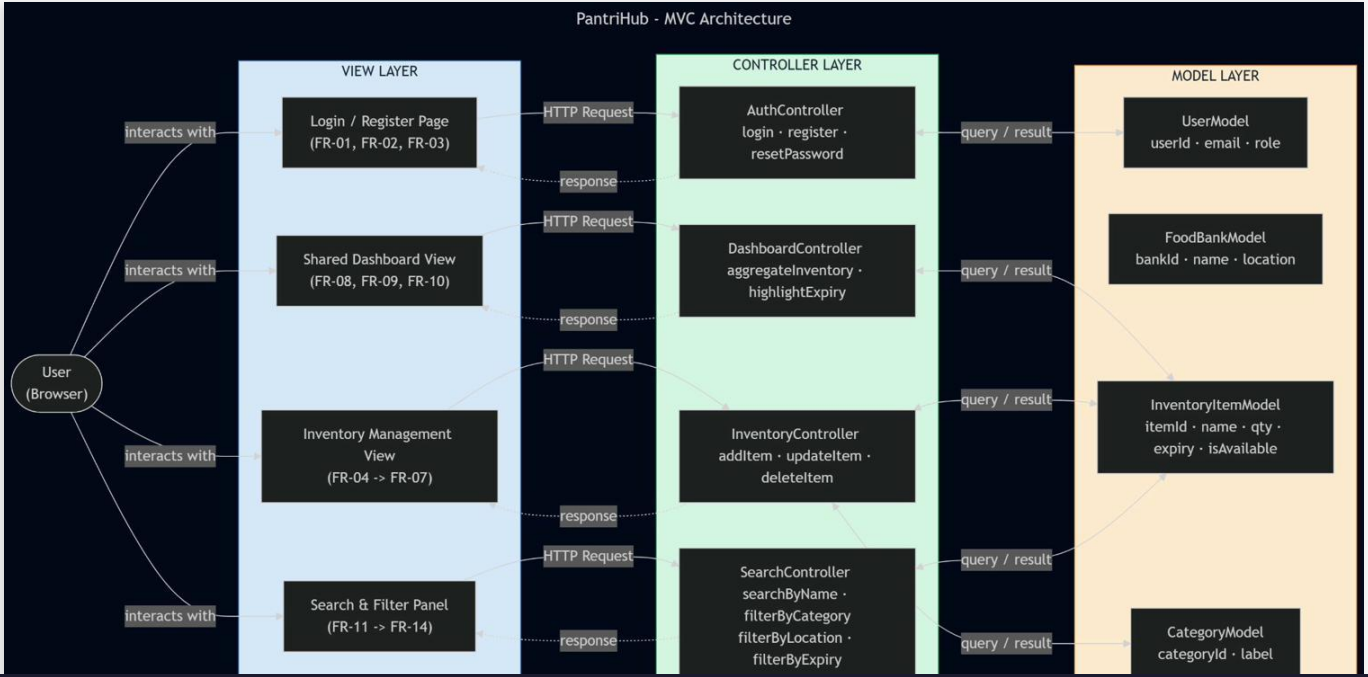

Node.js / Express • MongoDB • HTML / CSS / Bootstrap • JavaScript • GitHub

Work-in-Progress Demo

Project Structure
MVC folder organization (models/, views/, controllers/, routes/)

Complete

Sign Up / Registration Page
Frontend form with Bootstrap styling (FR-01, FR-02)

In Progress

Database Schema
MongoDB connection setup and initial schema design

In Progress

GitHub Repository
Version control, Kanban board, and documentation

Active

[LIVE DEMO HERE]

Next Week’s Plan

1	**Team Sync Meeting** Clearly assign task ownership, eliminate confusion	All
2	**Auth Backend (FR-01–FR-03)** Login, registration, session management	Ethan + Thomas
3	**Inventory CRUD (FR-04–FR-07)** Add, update, delete, mark availability	Ishan + Bushra
4	**Shared Dashboard (FR-08–FR-10)** Cross-location inventory view, expiry alerts	Shivam (flex)
5	**Regular Check-ins** Track progress, catch blockers early	All

Self-Reflection

How did we feel?

Academic conflicts made this week stressful, but seeing the registration page come together was motivating. We wish we had more time to commit to development.

What are we proud of?

Despite limited availability, Ishan and Bushra delivered frontend work, and Ethan moved the database setup forward. The team kept going without Shivam being present.

What did we learn?

Clear task ownership matters. When the lead is absent and assignments are vague, progress slows. We also learned that academic schedules need to be factored into sprint planning.

Going forward?

We will build in buffer time for academic conflicts, hold structured check-ins, and make sure every task has a single owner before a sprint starts.

Thank You

Questions?

github.com/bshra7/Inventory-Management-System-for-Food-Banks

PantriHub | ENSE 281 | March 2026
